



- ✓ NS Lands issues RFP “Former Landfill Site, Harrietsfield, Nova Scotia, Environmental Site Assessment” on August 1, 2018
- ✓ Contract awarded to AECOM – September 17, 2018
- ✓ Remedial Option Selected in March 2019
- ✓ Detailed Design and Environmental Approval work began April 2019 and completed in March 2020
- ✓ Leachate removal began in April 2020 and finished in September 2020 by GFL
- ✓ Construction contract awarded in fall 2020 to ARCP work commenced in September 2020
- ✓ Buildings demolished and buried debris areas began to be dug, sorted and placed in cell or trucked off site October 2020
- ✓ Exceeded off site disposal estimate amounts by more than 30% in December 2020
- ✓ Contractor shaped and placed run of bank grading and bedding material on cell in February 2021
- ✓ Contractor had to recondition grading and bedding material to meet specification
- ✓ Cap placement began in July 2021 and concluded in early October
- ✓ Groundwater diversion trench opened in October 2021
- ✓ ARCP Demobilized from site in December 2021
- ✓ Contract settlement in late February 2022



**Harrietsfield Remediation Project
Milestone Dates – Work Completed**

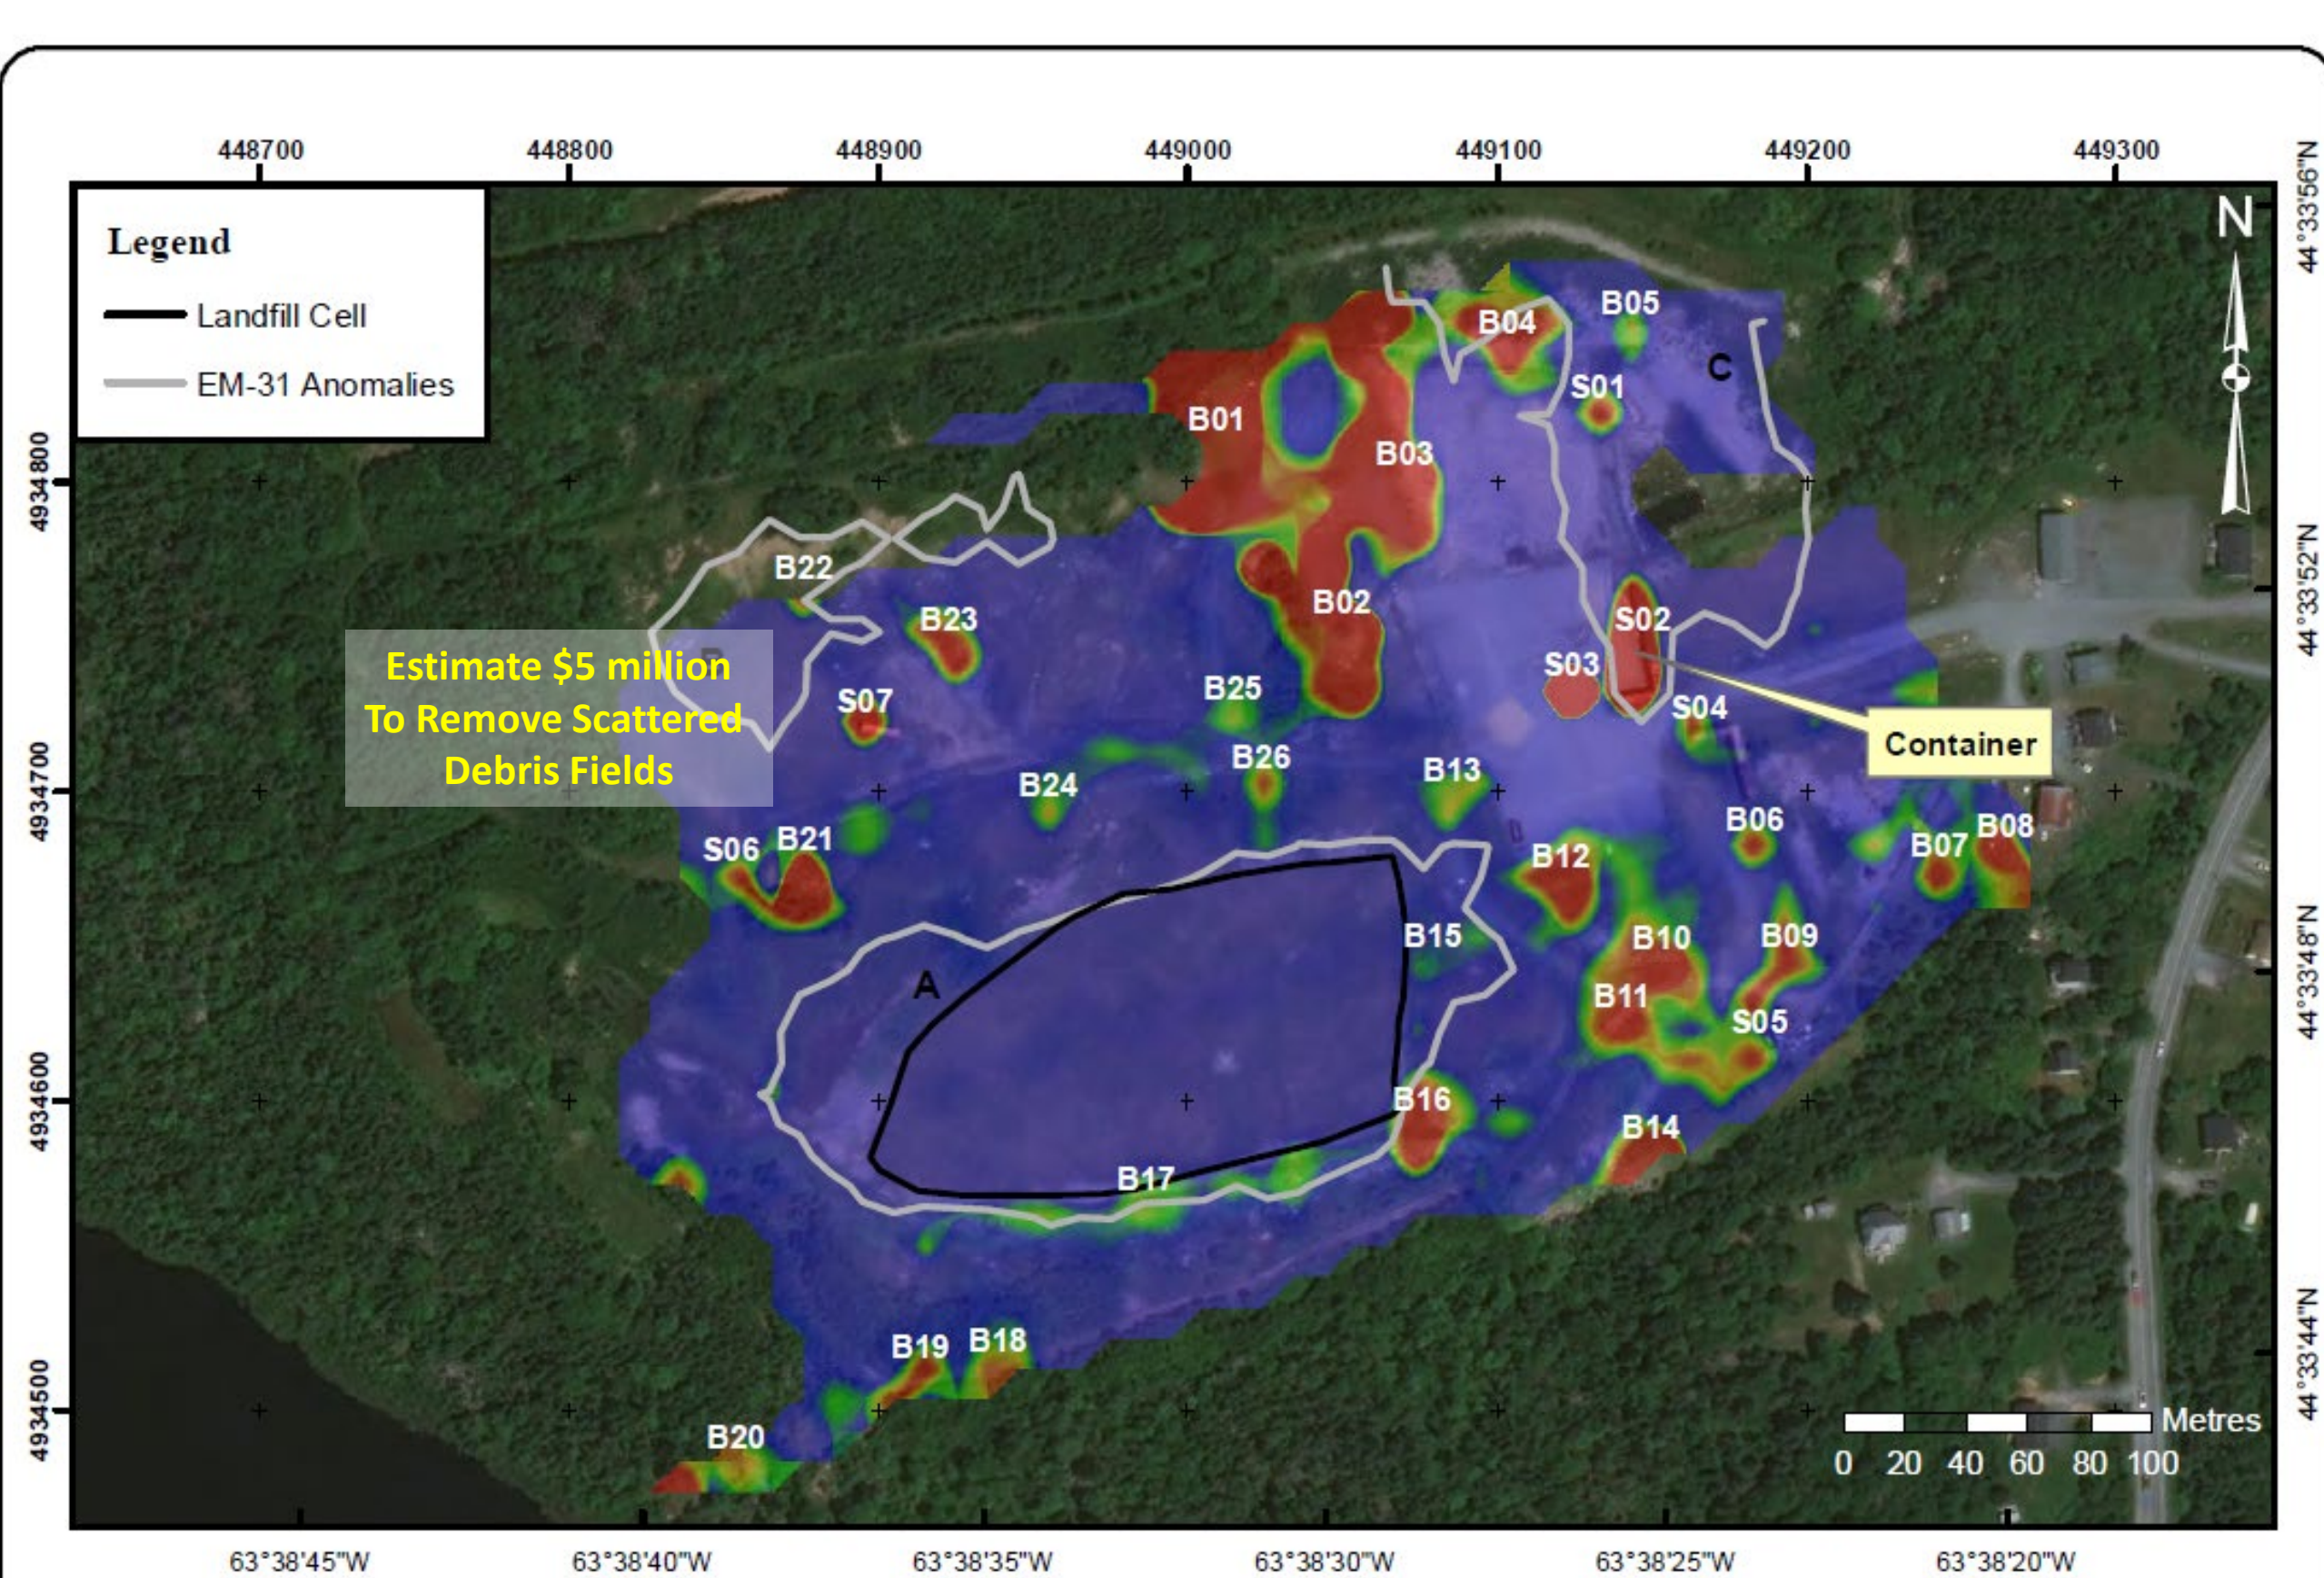


Figure 4.4.1: Shaded EM-61 anomaly map overlain with polygons outlining EM-31 conductivity anomalies.

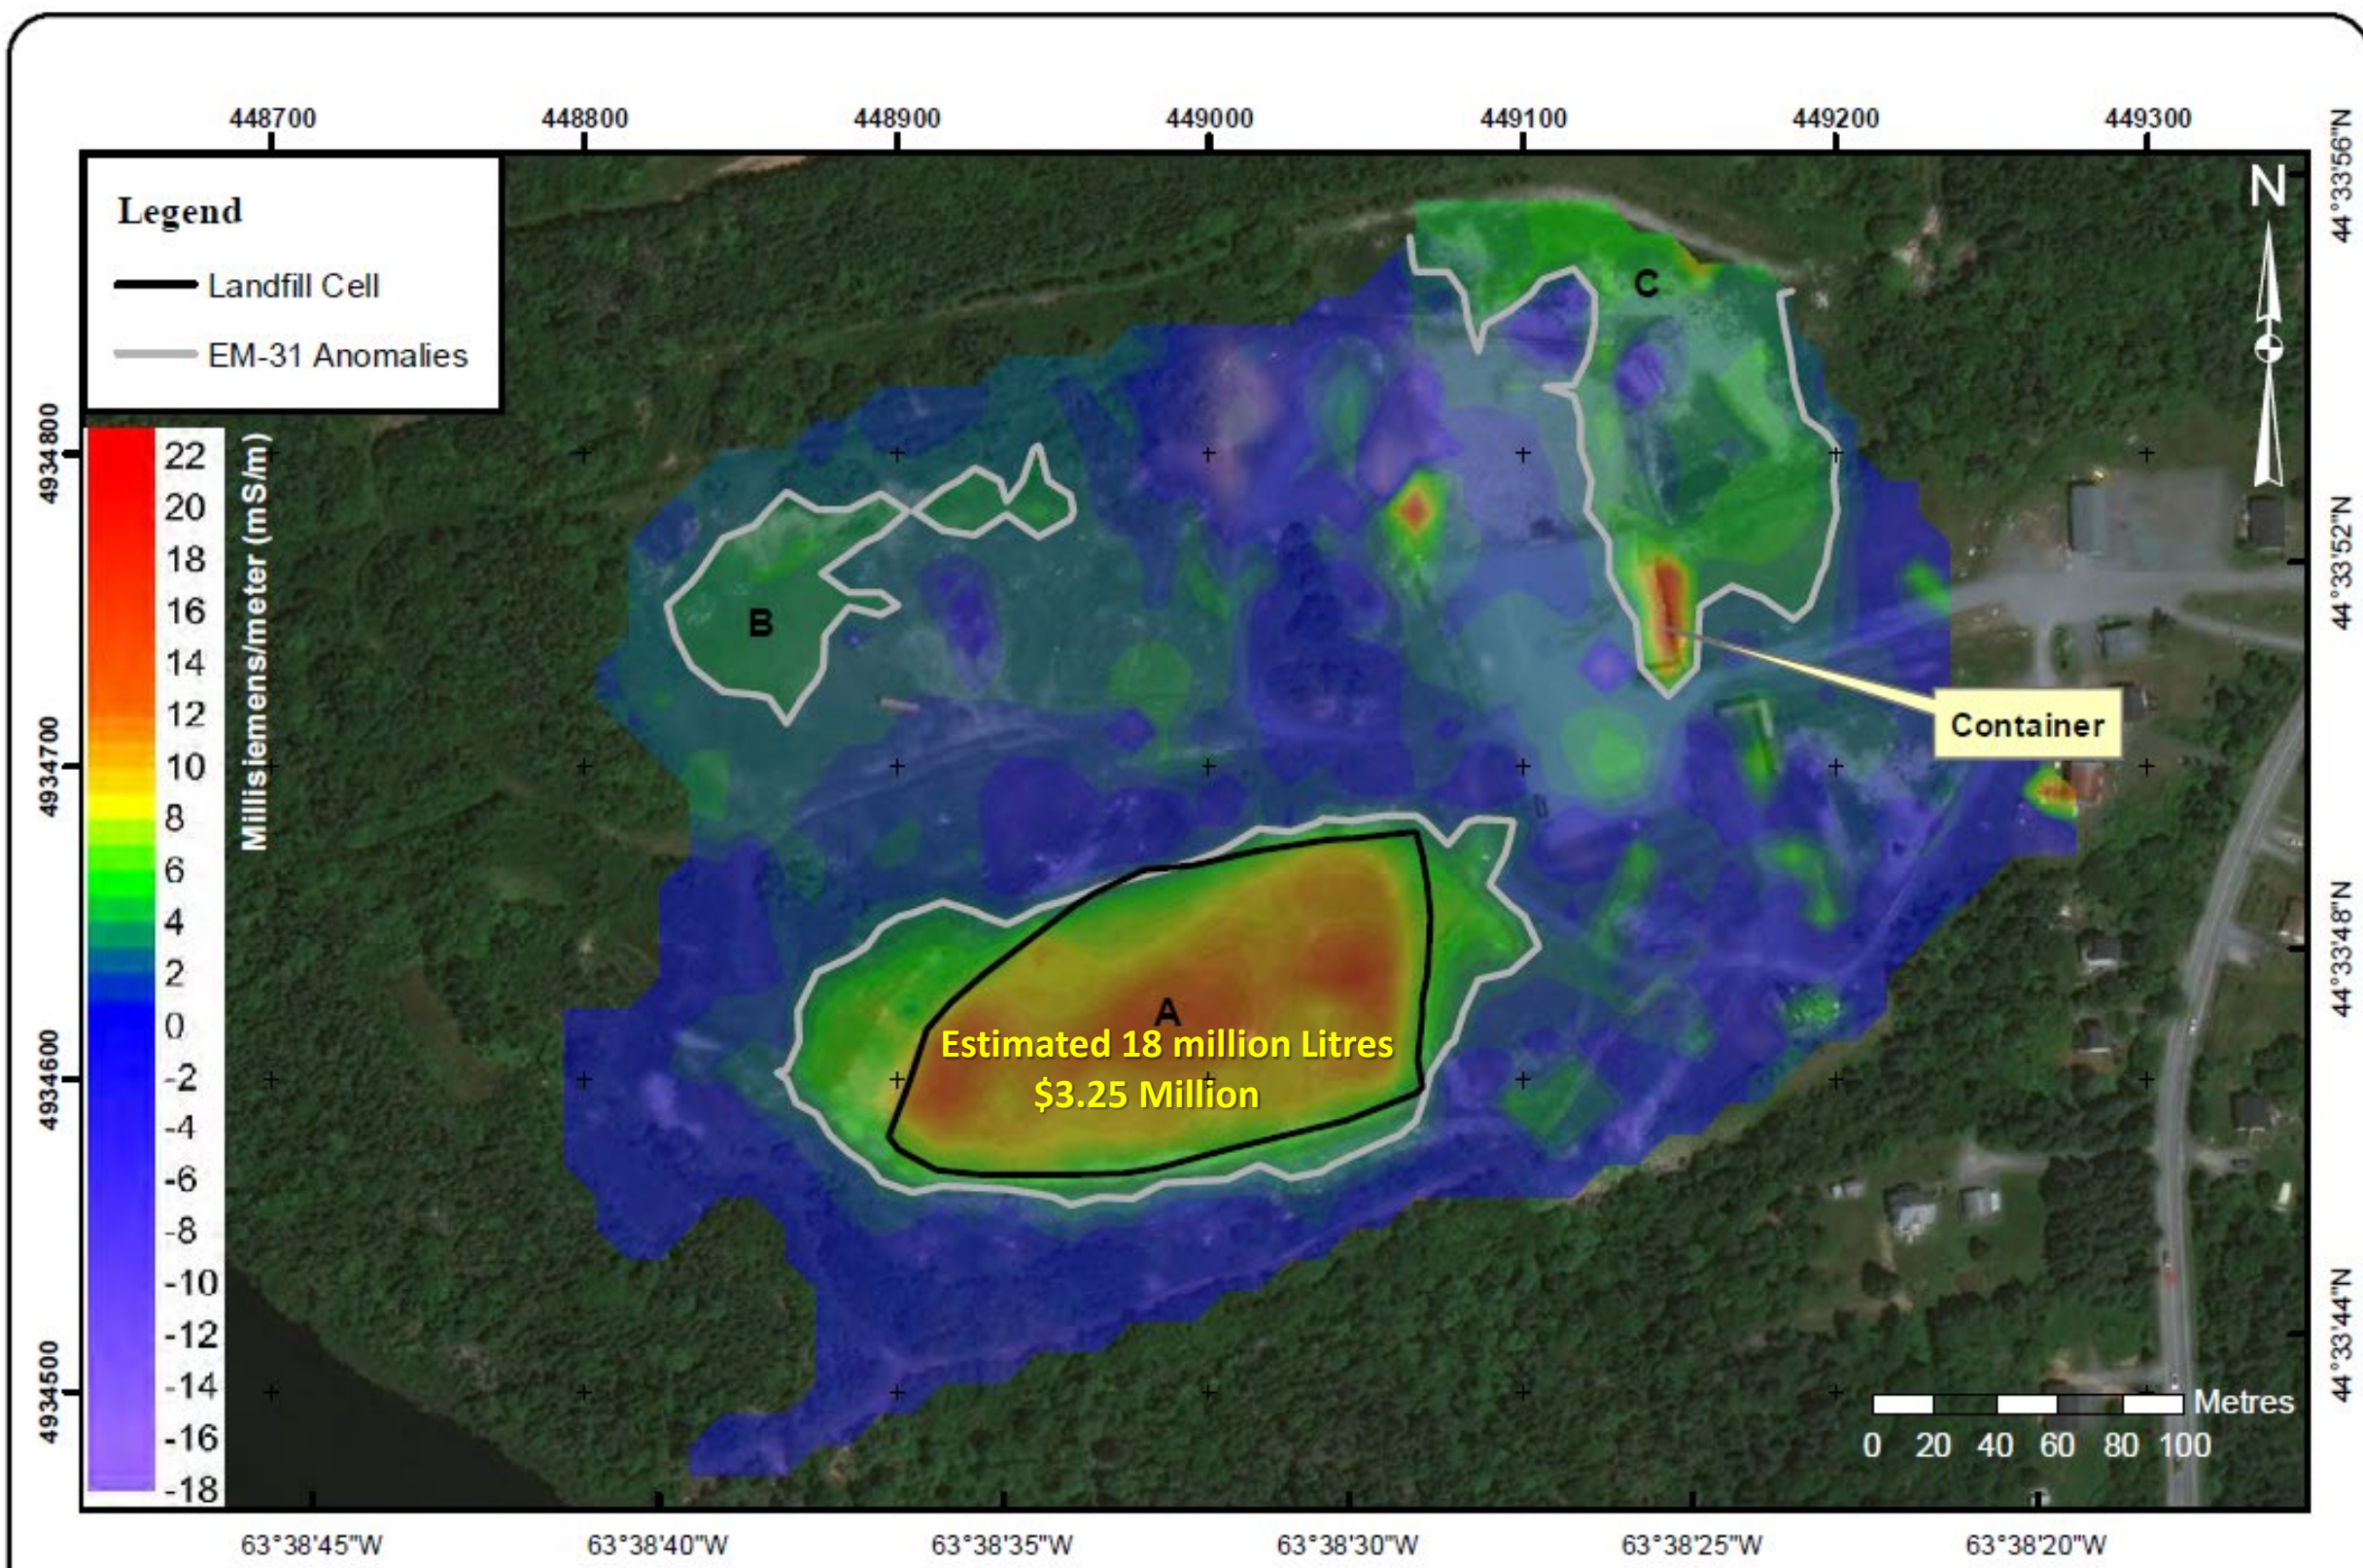


Figure 4.2.1: Vertical quad phase conductivity measured by the EM-31.

- NSECC began discussions with NSLI in December 2021 about taking over water treatment systems
- Site Professional Review of potential offsite impacts. Utilized NSE historical for impacted properties
- AECOM plan to sample and analyze water quality in relation to historic information and correlate back to RDM if possible
- After Year 1, offer recommendation on program for future
- Letters Issued for 3rd Party Monitoring and Notification March 15, 2022 for private well owners
- Agreement reached with Eco Water to extend one-year on March 15, 2022
- GFL on site to remove 1,000,000 litres of leachate from the cell prior to March 31, 2022
- Final Construction Report Due From AECOM on March 31, 2022
- Final Environmental Monitoring Report for Construction Activities Complete March 31, 2022
- Letters Issued for 3rd Party Monitoring and Notification March 17, 2022 for private well owners
- LTMM for the remediation site begins in April 2022 budgeted out for 25 years
- Tentatively planning Construction Completion Summary Meeting for End of April (NSLI/AECOM)
- Final ownership of the site to be resolved

2003



2005



2011



2013



